Mountain Lakes Behavioral Healthcare
16-Bed Residential Unit
Project Schedule
Project #25025

February 20, 2026
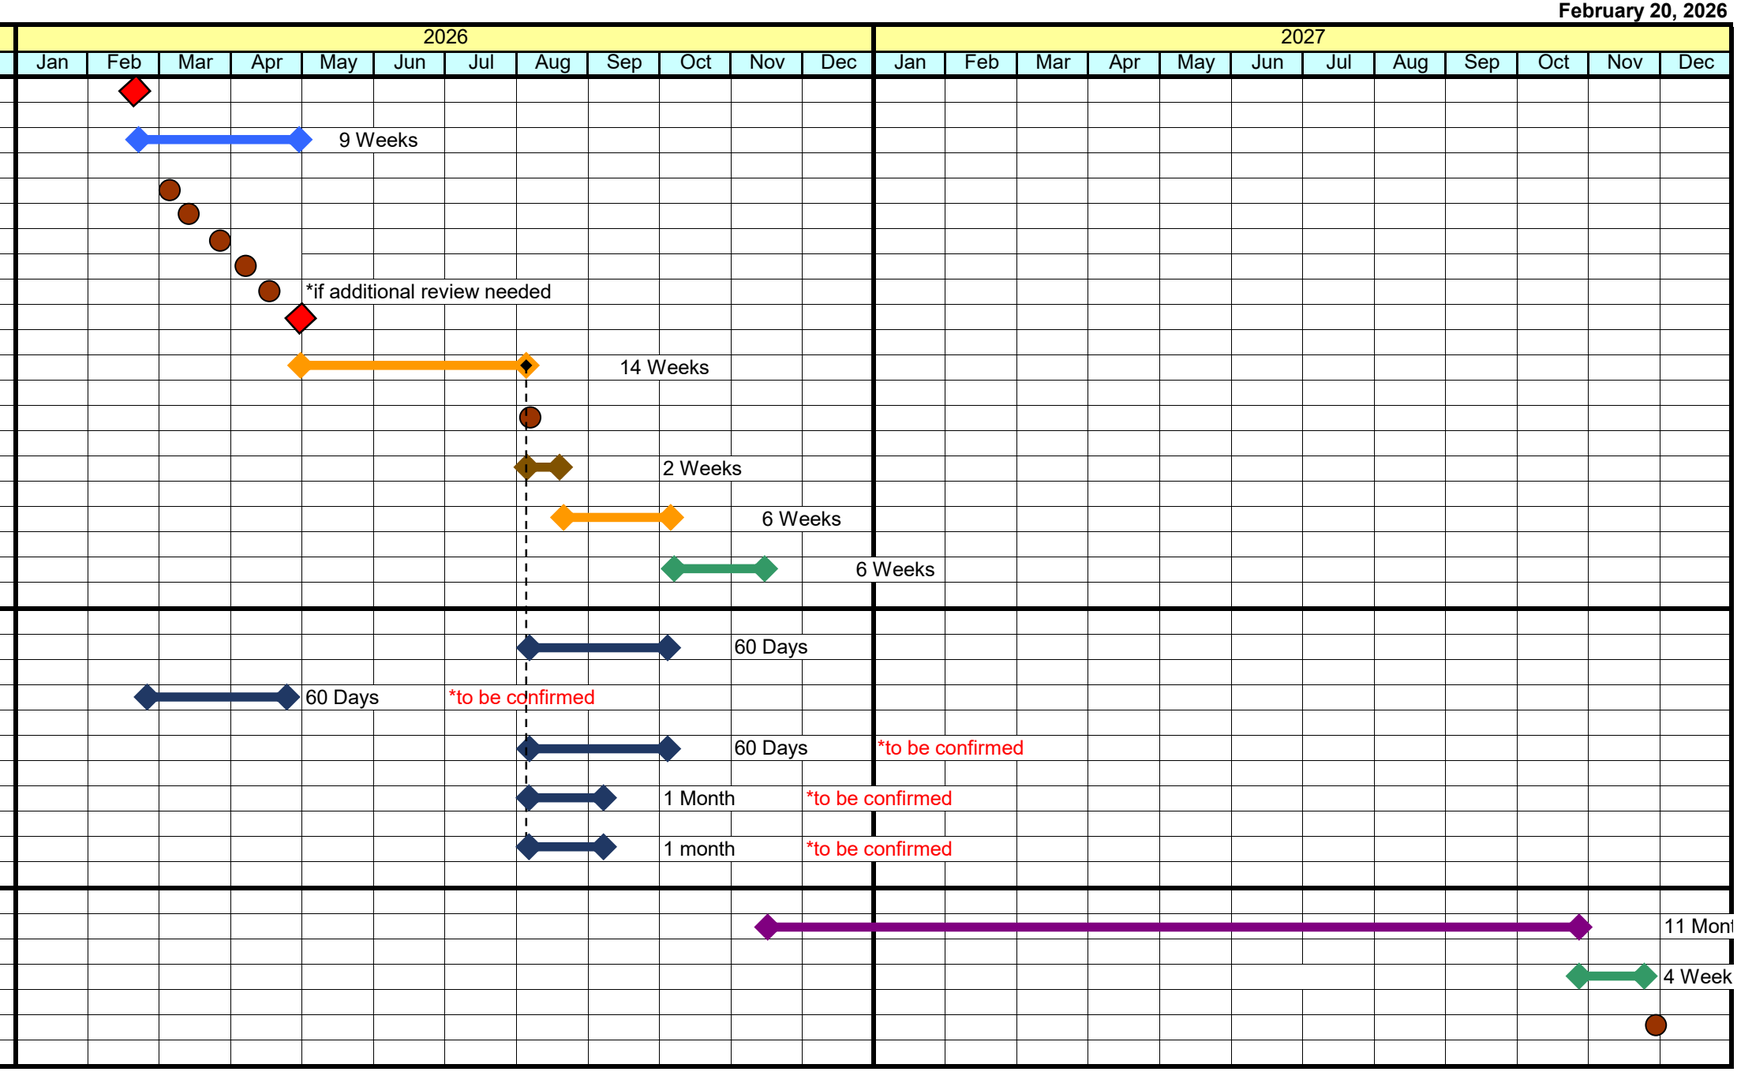
	Phase	Dates
Design	Owner Sign Off	2/20/2026
	Design Development	2/20/26 - 4/30/26
	Interiors Review	3/2/2026
	Finishes and Casework Review	3/9/2026
	Door Hardware Review	TBD
	Access Controls & Security Review	TBD
	User Group Meeting	TBD
	Owner Sign Off	Late April
	Construction Documents	5/1/26 - 8/5/26
	98% CD Package for AHJ	8/5/2026
	Checkset	8/5/26 - 8/19/26
	Complete CDs	8/19/26 - 10/2/26
	Pricing and Contract Award	10/5/26 - 11/14/26
AHJ	DMH Final Review	
	Zoning Preliminary Review (?) (Board of Adjustment = 6 Weeks)	
	Zoning Final Review (?)	
	Inspection Dept	
	Planning Commission	
Construction	Construction	
	CO & Move In	
	Occupancy	End of November 2027
